



**MUNICIPAL SEPARATE STORM SEWER SYSTEM (MS4)
ALABAMA AGRICULTURAL AND MECHANICAL UNIVERSITY
NORMAL, MADISON COUNTY, ALABAMA**

2022-2023 ANNUAL REPORT

**NPDES PERMIT NO. ALR040061
GEO SOLUTIONS PROJECT NO.: 17-0350**

**PREPARED BY:
GEO SOLUTIONS, LLC**



TABLE OF CONTENTS

1.0	INTRODUCTION	1
1.1	Permit History.....	1
1.2	MS4 Area	1
1.3	Hydrologic Units	1
1.4	Water Quality Concerns	1
2.0	CONTACTS.....	1
3.0	EVALUATION OF STORM WATER MANAGEMENT PROGRAM.....	2
3.1	Major Accomplishments	2
3.2	Overall Program Strengths and Weaknesses	3
3.3	Future Direction of the Program	3
4.0	MINIMUM STORMWATER CONTROL MEASURES.....	4
4.1	Public Education and Outreach.....	4
4.2	Public Involvement and Participation	4
4.3	Illicit Discharge Detection and Elimination	5
4.4	Construction Site Storm Runoff Control	5
4.5	Post-Construction Storm Water Management in New Development and Redevelopment.....	5
4.6	Post-Construction and Good Housekeeping	6
5.0	CERTIFICATION	7

APPENDIX A – SITE LOCATION PLAN

APPENDIX B – UPDATED STORMWATER SYSTEM

APPENDIX C – SPCC TRAINING POWER POINT SLIDES

APPENDIX D – LITTER POSTERS

APPENDIX E – STANDARD OPERATING PROCEDURES

APPENDIX F – BUILDINGS WITH POTENTIAL FOR ILLICIT DISCHARGES



1.0 INTRODUCTION

GEO Solutions has prepared the 2022-2023 Annual Report for Alabama Agricultural and Mechanical University's Municipal Separate Storm Sewer System (MS4) per the requirements of the Alabama Department of Environmental Management's (ADEM) National Pollutant Discharge Elimination System Permit (ALR040061). This report summarizes the programs accomplishments, events, monitoring and on-going storm water management.

1.1 Permit History

The United States Environmental Protection Agency (EPA) requires that all operators of small MS4s, as defined in 40 CFR Part 122.26(b)(16), maintain coverage for all storm water discharges. A Notice of Intent was submitted to ADEM in 2017 and MS4 Permit ALR040061 was issued on July 7, 2017. The permit was renewed effective October 1, 2021.

1.2 MS4 Area

Alabama Agricultural and Mechanical University is located in Normal, Alabama and is considered an entity within the City of Huntsville's city limits. The campus includes 2,300 acres with facilities for classrooms, student residences and athletic complexes. A map outlining the approximate boundary of the Alabama Agricultural and Mechanical University campus is included in Appendix A. There is one outfall located at 34°46'15.64"N, 86°34'56.72"W.

1.3 Hydrologic Units

The ultimate receiving water for Alabama Agricultural and Mechanical University MS4 is the Tennessee River (Region 06). The Subregion and Basin is Middle Tennessee Elk (06-03-00). The Subbasin is Wheeler Lake (06030002). The Watershed is Indian Creek (06030002-05) and the Subwatershed is Huntsville Spring Branch (060300020502). The onsite receiving water is Normal Branch which traverses the property from north to south.

1.4 Water Quality Concerns

The area that is covered under Alabama Agricultural and Mechanical University's MS4 Permit discharges at one single outfall, Normal Branch. Under Section 303(d) of the Clean Water Act, the State of Alabama is required to identify waterbodies that are not in compliance with the water quality standards for that particular use classification. Normal Branch does not discharge directly to an impaired waterbody. The stormwater layout for the MS4 permitted area can be found in Appendix B.

2.0 CONTACTS

The following personnel are directly responsible for the MS4 Program:

Mr. Brian Shipp
Director of Facilities and Administration
P.O. Box 1837
Normal, Alabama 35762
256-372-4276

Mr. Greg Bryant
Hazardous Environmental Manager
453 Buchanan Way NE
Normal, Alabama 35762
256-372-4090

Gregory.bryant@aamu.edu



Ms. Barbara R. Lehman, P.E.
Consultant
GEO Solutions, LLC
7201 Opportunity Boulevard
Huntsville, Alabama
256-837-6708
blehman@geo-solutions.net

3.0 EVALUATION OF STORM WATER MANAGEMENT PROGRAM

3.1 Major Accomplishments

Alabama Agricultural and Mechanical University was issued its first MS4 permit in July 2017 and is recognized as a small MS4 entity outside the City of Huntsville. The Department of Facilities and Administration was designated to oversee the storm water management program for the University.

Alabama Agricultural and Mechanical University only utilizes Proterra electric buses to the campus for the students and neighboring community to utilize to commute around campus bringing the total to five. By utilizing the cleaner and more efficient buses, the University is making a positive impact on greenhouse gas emissions with the Bulldog Transit System. Due to the reduction in need for diesel fuel, the University no longer requires additional above-ground storage tanks and containment areas for the buses.



A new and redesigned drainage system has been installed at the southwest portion of the campus. The area included the parking lot for the Foster Radiation Center. The contractor, SJ&L Construction Company performed the work in an effort to repair the eroded area and improve drainage.

The parking and drainage system has also been improved at the Old Buchanan Hall site. The improvements have improved the water flow from north to south on the northern portion of the property in an effort to prevent further erosion down gradient.

The construction of the Welcome Center and the Event Center are complete. The Event Center construction included a detention area on the south end of the project.





Road construction and drainage improvements are currently taking place across campus.

3.2 Overall Program Strengths and Weaknesses

One of the University's strengths this year has been the collaboration with the City of Huntsville's Green Team and Huntsville City Council.

The main weakness of the program continues to be staffing and funding.

3.3 Future Direction of the Program

During the upcoming year, Alabama Agricultural and Mechanical University plans to implement the following:

- The drainage features that traverses the western campus to the main outfall has plans for repair over the next year. The overall plans are currently being reviewed. The improvements will further stabilize the banks to prevent further erosion.
- The Alabama Agricultural and Mechanical University's website will continue to include links to tips and guidelines for storm water management on campus.
- With the complete transition to all electric mass transit transportation, the campus is moving towards the removal of the above-ground storage tanks.



4.0 MINIMUM STORMWATER CONTROL MEASURES

4.1 Public Education and Outreach

- Alabama Agricultural and Mechanical University's online publication, Bulldog Bottom Line, has been a major avenue for communication for the students and faculty. This online media will continue to be used in the future to encourage and educate the students regarding keeping the campus and the storm sewer clean with helpful reminders.



- Training - The Facilities Department conducted an annual training for Spill Prevention Control and Countermeasures for the Maintenance Department virtually. The training included Standard Operating Procedures in the Maintenance Shed as well as around campus. The trainees reviewed the types of spills, how to identify a spill, how to clean up spills and how to avoid them. Several scenarios were presented for the trainees to demonstrate their understanding of the plan. The Power Point Presentation for the training is included in Appendix C.

4.2 Public Involvement and Participation

- Signs and Posters - Alabama Agricultural and Mechanical University provided the signs, posters and their messages on the Bulldog Bottom Line. Copies of the posters can be found in Appendix D.
- The University has an Environmental Department that includes faculty, as well as students, who are involved in activities on and off campus. The student body has teamed up with the City of Huntsville's Green Team to collect litter at District 1 Cleanup Day. Safety vests, gloves, grabbers and garbage bags were provided to the students to collect litter in the surrounding neighborhoods.
- More than 500 freshmen were involved in "Serving the City as One" in several neighborhoods in North Huntsville. Students and community volunteers gathered at T.M. Elmore Gymnasium on the University's campus before loading buses to work in the areas of Edmonton Heights, South Plymouth Road, Merry Oaks Drive, Esther Avenue and The AAMU Farm in Hazel Green. The service included, but not limited to, clearing yards and making small home repairs. The event was in collaboration with Huntsville City Council Member Devyn Keith and Madison County Commissioner Violet Edwards.



- The Alabama Agricultural and Mechanical University's student body is participating in the state wide Adopt-a-Mile Program. The mile is along Chase Road which traverses on the southern perimeter of the University's campus. During their routine checks and maintenance, the students clean up trash and litter to aid in the ongoing beautification of the city.

4.3 Illicit Discharge Detection and Elimination

- Aerators - There are two ponds on the Alabama Agricultural and Mechanical University Campus. Both of the ponds have aerators to increase the oxygen saturation.
- Hazardous Materials – Mr. Greg Bryant is the Hazardous Environmental Manager and conducts routine inspections looking for and documenting hazardous material on campus.
- SPCC – A Spill Prevention Control and Countermeasures Plan was developed for the Alabama Agricultural and Mechanical University Campus. There are two above-ground storage tanks located at the Maintenance Shed, as well as used oil containers. Several of the buildings on campus have back-up generators. The maintenance staff has received training on the Standard Operating Procedures when there is a spill.
- Standard Operating Procedures for the SPCC Program, Illicit Discharge, Construction and Post Construction were developed and a copy can be found in Appendix E.
- There are numerous buildings with potential for illicit discharges. A list of the buildings and the possible generators can be found in Appendix F.
- The new construction, the Event Center and the Welcome Center, do not include water coolers. They will utilize a close-looped chiller system.

4.4 Construction Site Storm Runoff Control

- Construction Storm Water Permits – There is still one Construction Stormwater Permits under the NPDES General Permit. The New Event Center is permit ALR10C07N; the Responsible Official is MJ Harris Construction Services. Regular inspections are conducted per ADEM's permit requirements by a QCI as well as a representative of Alabama Agricultural and Mechanical University.
- Monthly and rainfall driven inspections are conducted by Mr. Greg Bryant, Hazardous and Environmental Manager for Alabama Agricultural and Mechanical University as well as a third party, GEO Solutions, LLC. Records are kept in the Facilities Building on campus.

4.5 Post-Construction Storm Water Management in New Development and Redevelopment

- Landscape Management - Aramark Higher Education Services is subcontracted by Alabama Agricultural and Mechanical University to provide landscape services to the campus. They ensure that the drainage ways remain unblocked to prevent unnecessary ponding or backing up of storm water. Due to the highly erodible soils located on the campus, Aramark is responsible for stabilizing the bare areas.





Welcome Center



Event Center


4.6 Post-Construction and Good Housekeeping

- Aramark collects and removes all of the trash on a daily basis around campus. They also are responsible for major maintenance and managing the interior roadways. Approximately twenty-four bags of trash are collected daily around the campus.
- Regular inspections are performed across the campus to monitor trash pick-up and general maintenance.
- Use oil from maintenance vehicles and equipment is removed from the campus and disposed of by a third party.



5.0 CERTIFICATION

I certify under penalty of law that this Annual Report and all attachments pertaining to the Alabama Agricultural and Mechanical University's Municipal Separate Storm Sewer System were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information including the possibility of fine or imprisonment for knowing violations.




Mr. Brian Shipp, Director
Facilities and Administrative
Alabama Agricultural and Mechanical University

5/31/23
Date



APPENDIX A

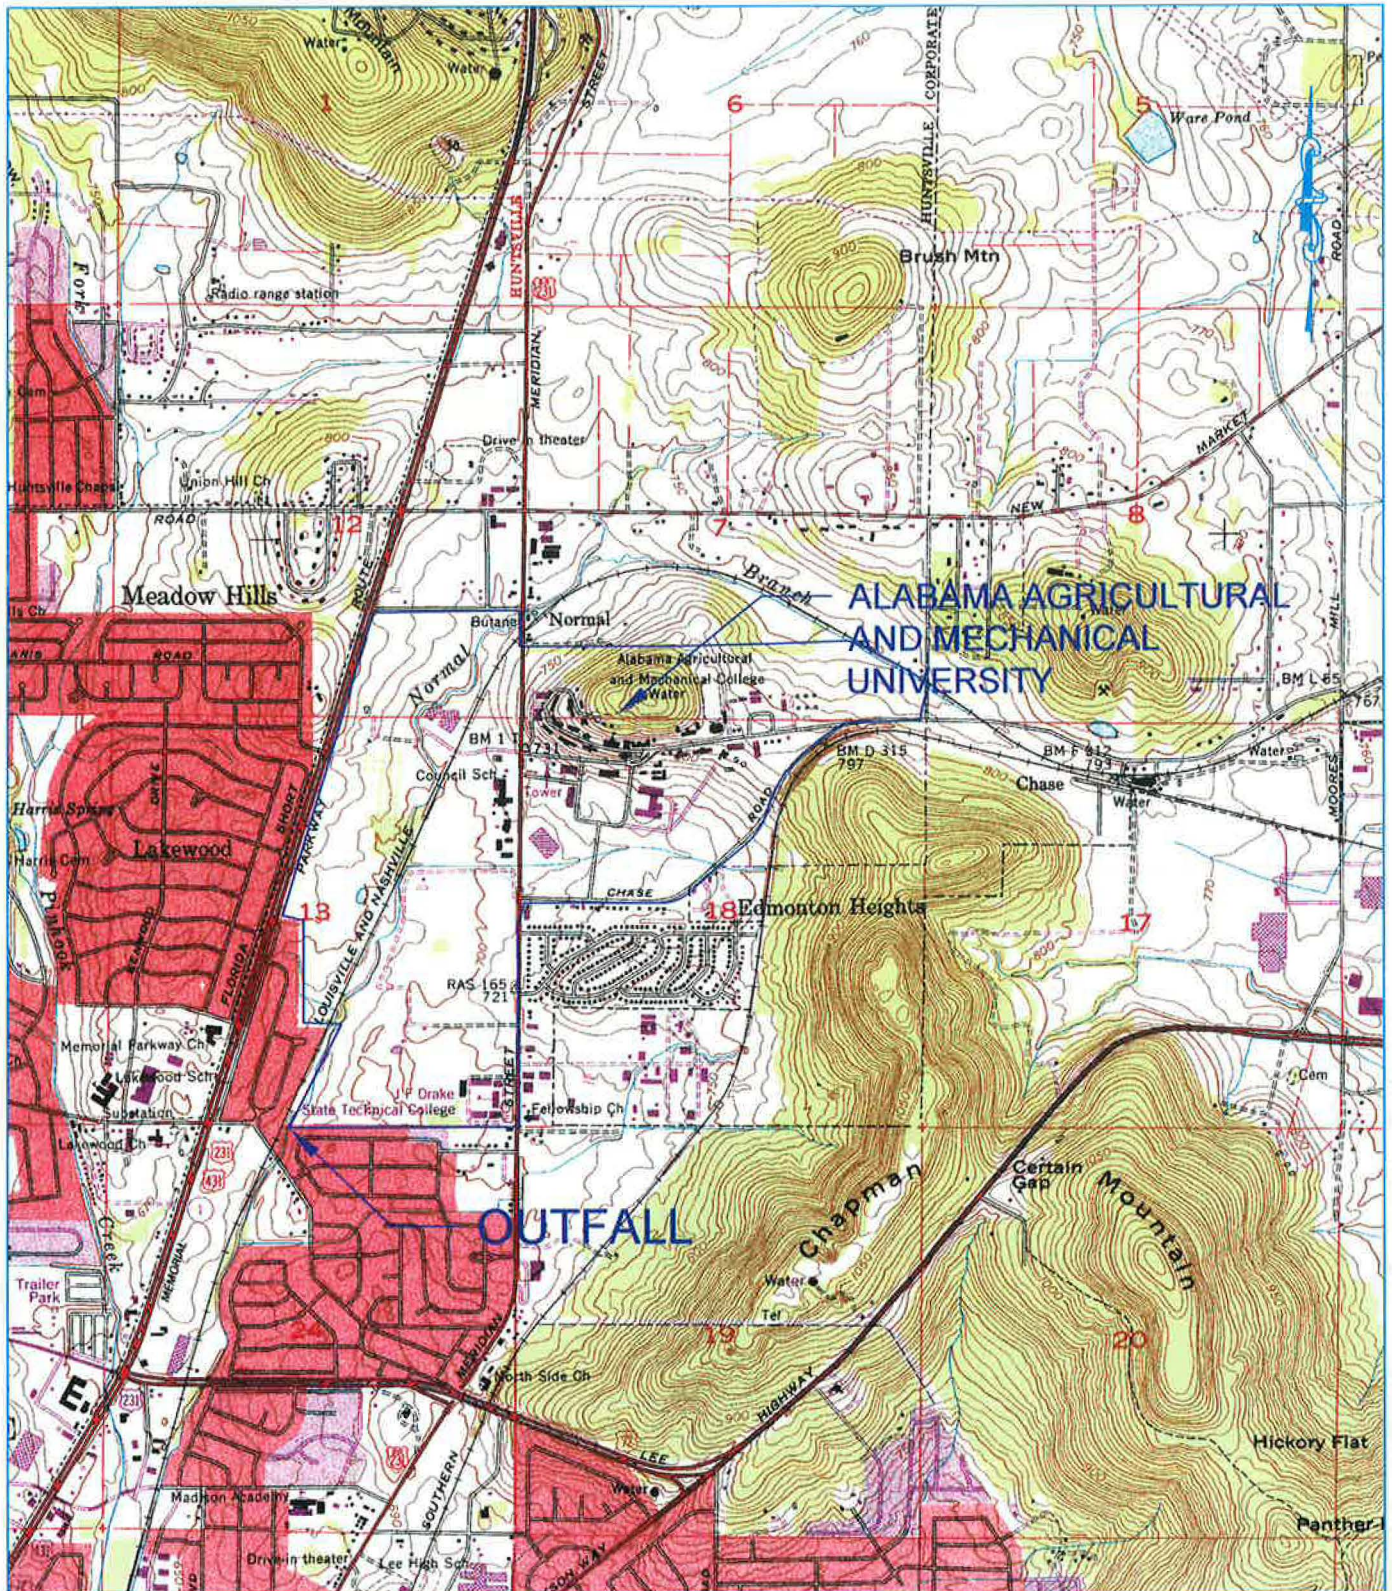

ALABAMA AGRICULTURAL
AND MECHANICAL
UNIVERSITY
NORMAL, ALABAMA

FIGURE 1
SITE LOCATION PLAN



7201 Opportunity Boulevard
Huntsville, Alabama 35810
PH (256)837-6708 FX (256)837-6702

SCALE: 1" = 2500'


PROJ: 17-0350

DATE: 5/31/2023

1 OF 1

APPENDIX B

Stormwater Systems Around AAMU

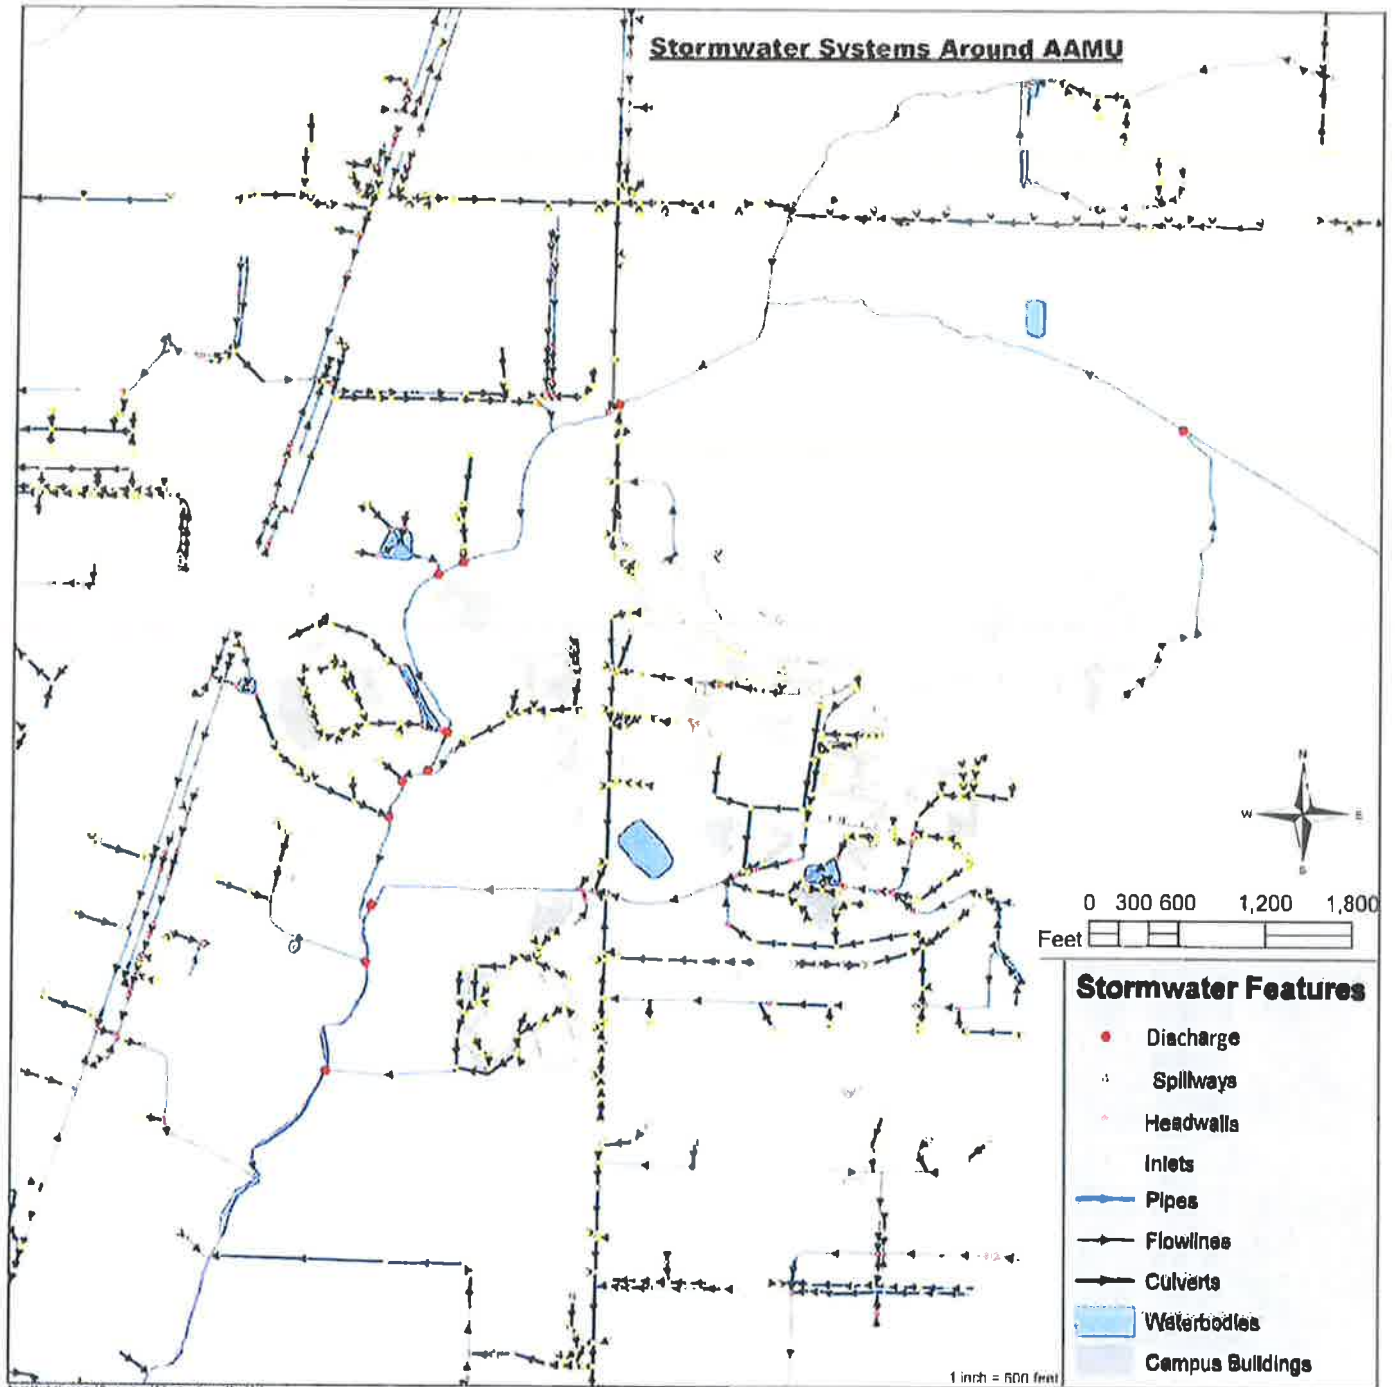

APPENDIX C

Spill Prevention Control and Countermeasures

SPCC Federal Requirements



SPCC Federal Requirements

The Federal Clean Water Act specifies the requirements for SPCC Plans

The Code of Federal Regulations 40 CFR 112 details requirements of the SPCC Plan

The SPCC regulations establish procedures, methods, and equipment needed to prevent oil discharges into waters of the United States



SPCC Federal Requirements

A facility is required to have a SPCC Plan if it has:

Total above ground oil storage of more than 1,320 gallons; AND

There is the potential for oil to reach streams or other water bodies

Alabama A&M University meets these requirements and therefore is required to have a SPCC Plan



Alabama A&M University

SPCC Plan



Alabama A&M University SPCC Plan

The Alabama A&M University SPCC Plan is kept on file at the Environmental Health & Safety Office located at Physical Facilities Building.

The document was prepared and certified by a Registered Professional Engineer.




Alabama A&M University SPCC Plan

The Alabama A&M University SPCC Plan includes:

- Description of oil storage locations
- Description of secondary containment for oil storage
- Locations of spill clean-up and containment materials
- Maps or other information to indicate where a release will migrate
- Spill history, potential spill sources, and spill prevention techniques
- Spill Response/Clean-Up plan
- Other applicable guidelines

Training Requirements for Spill Prevention Control and Countermeasures (SPCC) 40 CFR Part 112

ALABAMA A&M UNIVERSITY



Goals of SPCC Training

- To familiarize employees with the written SPCC Plan
- To help employees identify oil storage locations and loading procedures
- To assist in identifying spill pathways
- To provide a discussion of spill prevention procedures
- To familiarize the employee with appropriate spill response procedures and use of spill response equipment.

Types of Oil Which May Be Regulated Under the SPCC

All petroleum based oils.

Fuel Oil, Gasoline, Hydraulic Fluid, Motor Oil, etc.

Animal fats and oils.

Fish and marine mammal oils

Vegetable oils

All the above oils mixed with wastes

Never mix used oil with other wastes



Oil Storage at Alabama A&M University Included in SPCC Plan

Oil Storage at Marquette University includes;

Aboveground Storage Tanks (ATS)

Waste Oil Collection Station

55 Gallon Drums in various locations





Gasoline and Diesel Fuel for Vehicles and Equipment



Used Oil Storage



Diesel Back-Up Generators

Main Elements of the SPCC Plan

Operating Procedures implemented to prevent oil spills.

Examples: Regular inspections, SPCC On-Site Coordinator observing tank filling procedures.

Control Measures installed to prevent oil from reaching navigable waters.

Example: Secondary containment.

Countermeasures to contain, cleanup, and mitigate the effects of an oil spill.

Examples: Cleanup and spill equipment availability on site, available list of contacts and phone numbers for employee use during spills.

SPCC Program Goals

Spill Prevention

Installation of proper equipment, repair of malfunctioning systems, inspections, and good fueling and handling practices

Spill Control

Monitoring of leak detection, proper reporting, inspection of containment and piping systems.

Spill Countermeasures

Quick, proper, and safe response to spills.



Potential Spill Pathways

In some areas, oil can enter the “Navigable Waters or adjoining shorelines” by:

- Direct spillage into a storm drain.

- Never allow oil to drain into an open drain or into a ditch or waterway.

- Oil containing equipment (i.e. a vehicle) is never to be rinsed or washed near a storm drain or waterway.



Spill Scenarios (Large Release)

Damage to or accidental release from oil delivery equipment during loading or unloading of oil at fill ports of storage tanks.

Catastrophic Tank Failure and Leaving Secondary Containment

Fuel tanker failure during delivery

Motor vehicle accident involving oil delivery equipment.



Spill Scenarios (Small Release)

Small overflow at fill port of fuel tanks.

Spillage of oil during transfer to or from drums and tanks.

Leaking and or failure of pipes and pumps.

Leaking and or failure of drums.



Spill Prevention

Routine Inspections

Our site specific SPCC plan includes the frequency schedule and checklist necessary for proper inspection.

Ensure that necessary maintenance and repairs are completed as scheduled and recorded.

SPCC specific inspections are conducted on a Monthly basis.

Inspection records must be kept for a minimum of three years

Secondary Containment

Definition of proper containment

All bulk storage containers of oil must be located in containment sufficient for the entire capacity of the largest container and sufficient have sufficient freeboard to contain an additional 10% volume.

Secondary containment must be impervious material

Secondary containment is **NOT** required for Qualified Oil-Filled Operational Equipment such as transformers or electrical switches currently in use.

Secondary Containment

Routine Inspection

Can be performed by any SPCC On-site Coordinator.

Check for indication of oil leaks on floors, pallets, dikes, retaining walls, and berms.

Water must be able to drain out **ONLY** if there is no noticeable sheen.

Refer to your site specific SPCC plan for specific details regarding your site's secondary containment inspection.

Secondary Containment



Spill Response

Discovery of Release

Contact EHS or Aramark Manager
Alabama A&M EHS Contact is

Gregory A. Bryant

Office Phone 256-372-4090

Cell Phone 256-924-0249

Extinguish or remove any source of ignition.

Identify the material and its point of release.

Attempt to **stop the release** at its source if it is safe to do so.

Spill Response

Discovery of Release cont.

Contain material to prevent release into the environment

Initiate the spill reporting procedure as specified in your site specific SPCC plan

Recover or clean up spilled material

Decontaminate tools and equipment

Arrange for disposal of waste materials through EH&S

EH&S is responsible for reporting to outside agencies.

Spill Response

For “large spills” that can’t be controlled by in-house personnel and materials contact:

Tradebe Environmental Services

EMERGENCY RESPONSE

1-888-276-0887



Spill Reporting

For a spill over 25 gallons that occurs the Service Manager (Aramark) or EHS will have to report to the following agencies NOTE : EHS will do the reporting unless unavailable.

ADEM – Decatur Field Ops (7AM – 5PM) 256-353-1713

Dept. of Public Safety (5PM – 7AM) 256-242-4378

Spill Reporting

Documentation

The following information will need to be provided when reporting

Name of person reporting release/spill

Company

Mailing Address

Telephone Number

Location of Spill

Description of what is release (ex diesel fuel)



Spill Reporting

Documentation cont.

Estimated amount

Source or the spill (where it came from)

Cause of the spill

Nearest receiving water way



After a Spill

A Spill Report will be completed by EHS and filed with the EHS office

Relevant information such as initial information, pictures, clean up information

Be sure to include information on:

- How to prevent another occurrence

- Effectiveness of the response

Remember to restock your spill kit with any used items and/or add items that may be useful in the future if warranted.



Spill Response Supplies

Floor (Oil) Dry

Shovels, brooms, and dust pans

Spill Kit:

Absorbent booms, pads, and socks

Protective gloves and safety goggles

Caution tape

Collection bags

Labels



Location of Spill Response Supplies

Spill response equipment will be located at fueling location in a water proof container.

EHS will help provide replenishment of clean up supplies.



SPCC Resources

EPA SPCC Management Guidelines

<http://www.epa.gov/emergencies/content/spcc/index.htm>



Questions?

Alabama A&M University Department of Environmental, Health & Safety

Please contact me at 256-372-4090 with any questions or concerns that you may have.



APPENDIX D

KEEP OUR CAMPUS CLEAN!

Litter!



Pointless Personal Pollution



IT KEEPS OUR WATER CLEAN

Storm Drains Are Not Trash Cans



Trash thrown in storm drains travels into our streams and disturbs aquatic life. Trash can also clog storm drains and cause flooding. Dispose of your trash properly, not in the storm drain.



Healthy Stream Habits!



APPENDIX E

Illicit Discharge Detection and Elimination (IDDE) SOP

Alabama A&M University goal is to develop a plan to identify and eliminate non-storm water discharges that are not acceptable according to the MS4 General Permit. The university has installed in the case of one being discovered as regulatory means to correct the actions.

1.1 Reporting a IDDE

Illicit Discharge are reported by individuals on campus by calling EHS office number 256-372-4090. IDDE can be detected through inspections around campus

1.2 Tracing Illicit Discharges

Once an illicit discharge is detected or reported through an inspection. The next step is to locate the source. Selection of tracing techniques will depend on the type of illicit discharge detected, information collected during the initial discovery period, observation, and the resources/technology available. Tracing techniques include visual observation, dye testing, sample collection, and televising

Various techniques can be used in combination to identify the source of the illicit discharge.

- **Transitory or intermittent discharges**: These conditions may occur as a result of an inspection or a community complaint. While initial information may have been collected regarding the potential illicit discharge, a return trip may show that the discharge was either intermittent or transitory. The investigative techniques used will depend on whether or not a potential source location was identified during the initial observation:
- **Potential source identified** - If a potential source for the illicit discharge was initially identified, steps are taken to investigate the potential source site, such as inspecting the site and storm drain system in the vicinity of the site. If floor drains, sumps, or other suspect discharge locations are observed during this inspection, dye testing, smoke testing, or continuous flow monitoring may be used. These techniques should definitively show whether the suspect site was the source of the illicit discharge.



- **Potential source not identified** - If no source site is suspected, and only the general area of the illicit discharge is known, it may be possible to trace the evidence of the illicit discharge by visual inspection of the storm drain access points. If this catch basin/manhole inspection technique is unsuccessful, some interim steps may be taken to attempt to capture water from an intermittent discharge. For example, sand bagging, damming or block testing of selected storm drain access points, combined with installation can help reveal the source of the discharge. If these techniques have no positive result (no water pools behind the weir or sand bag), the discharge was likely transitory (one time only), and it may not be possible to determine its origin. and should be logged tracked for any future incidents.
- **Continuous discharges**: Tracing continuous discharges is typically easier than tracing transitory/intermittent discharges. The primary difference between tracing this type and tracing a continuous discharge is that sandbagging and weirs are not required for a continuous discharge. Visual observation of the system access points should reveal where the flow is coming from. If visual inspections fail in identification of the source and the original report was severe or gross pollution, then televising, smoke testing, or sample collection would be warranted

1.3 Regulatory Mechanism

If Alabama A&M University discovers the violation of the IDDE SOP. The individuals or companies may require verbal or written notice for non-compliance

- The performance of monitoring, analysis and reporting
- The termination of the prohibited discharge, practices, or operations
- The abatement or remediation of the storm water pollution, and the restoration of the affected property
- Payment of non-compliance fees or remediation expenses against Alabama A&M University
- Disciplinary action up to and including dismissal of personnel or contractors



Dry Weather Screening SOP

Alabama A&M University shall, at a minimum, visually inspect outfall annually during dry weather conditions.

- Flows suspected of containing illicit discharges due to the presence of odors, colors or sheens shall be investigated.
- Investigation may include water chemistry field testing and/or bacteriological sampling and will be dependent upon the characteristics of the observed discharge. Investigations will involve Facilities Management Contractor to trace source of suspect illicit discharge.
- Upon source discovery, measures will be implemented to cease discharge immediately as possible.
- Should immediate termination not be practicable, a schedule will be developed.
- Should the source of discharge be determined to originate off campus, the MS4 community having jurisdiction will be notified within 24 hours as well as the Department.
- The physical condition of the outfall shall also be noted during the inspections.



Construction Storm Water Runoff Control SOP

Alabama A&M University goal control construction storm water runoff by implementing plan site reviews, control mechanisms, an inspection.

- **Site Plan Review**

Physical Facilities Department are responsible overseeing all construction projects conducted on campus. The department is responsible for assuring storm water runoff controls are implemented prior to construction. This can involve review of architecture's site plans and construction specifications

- **Sites Less than 1 Acre is Disturbed**

Construction sites where less than one acre of ground is disturbed will be covered on AAMU MS4 General Permit and BMP's. The contractor will be responsible implementing control mechanisms, i.e. silt fences, inlet protection, street sweeping.

Alabama A&M University will at a minimum perform an inspection of site every two months to ensure the BMP's and control mechanisms are being implemented.

Any deficiencies noted during these inspections will be presented to the construction superintendent or project design engineer or architect.

- **Sites More than 1 Acre is Disturbed**

Construction site where more than 1 acre is disturbed or part of a large development Alabama A&M University requires the contractor to obtain ADEM Construction Storm Water Permit and follow all applicable requirements of the permit.

Copies of the permit and inspections will be sent to the EHS department as part of compliance with requirements of the inspection.

Alabama A&M University will perform at a minimum perform monthly inspections to ensure control mechanisms and monitoring issues are in place.

Any deficiencies noted during these inspections will be presented to the construction superintendent or project design engineer or architect.

Re-inspections could be required to these issues have been corrected.



Post Construction Storm Water Management SOP

The goal of the university's post construction runoff control measure is designed to ensure that new construction designs do not result in increased storm water pollution.

- As part of the site plan review, Alabama A&M University reviews site plans, specifications, design plans on post construction designs.
- The general contractor for all projects are required to implement post construction design for any undisturbed acre. This applies to projects less than and greater than one acre in design.
- Post construction control mechanisms are grass seed and straw, sod, and landscaping (i.e. shrubs, trees, mulching). These are some of the steps to be implemented to slow down and improve runoff water quality.
- Construction control mechanisms will stay in place until, the post construction designs are fully in place.
- This includes significant grass coverage 85% percent at a minimum. Sod has begun to root and grow. Control mechanisms will only be removed if the university feels that exposed ground surfaces have been adequately stabilized.
- Once the project is turned over to the university, Physical Facilities ground's and maintenance contractor is responsible for maintaining the post construction controls.
- The university will ensure the post construction implementations are maintained and point out any deficiencies to the contractor.



Housekeeping SOP

The goal of the university is to practice good housekeeping skills to help keep the drainage areas free from debris and trash.

- Facilities contractor, Aramark pick up trash every morning M-F primarily while school is in session. Aramark spends approximately 2-3 hours pick up trash and disposing it properly.
- Aramark also works on keep landscaping areas covered to prevent storm water runoff and wash out areas.
- Trash containers area keep free trash to prevent trash from getting in drainage culverts and outfall
- Drainage culverts are cleaned out by outside contractors when they present issue with improper drainage.
- **Regulatory Mechanism**

Records will be kept for any clean out or repairs done storm drain culverts.

Trash pick-up and landscaping are part of the operating procedures and contract requirement of the Facilities vendor, Aramark.

Any deficiencies noticed will be pointed out by the contractor and follow up for other work will done if needed.



APPENDIX F

Buildings With Potential for Illicit Discharge

	<u>Boilers</u>	<u>Diesel Generators</u>	<u>Water Cooling Towers</u>	<u>Labs</u>	<u>Other*</u>
Ag. Mechanics Crump Building	X				
Agribition Center	X				
Agriculture Research ARC	X			X	
Auther J Bonds School of Engineering	X	X	X	X	
Carter	X	X		X	
Carver	X			X	
Chambers	X	X			
Council Training	X				
Crump maintenance building	X				
Dawson	X				
Eugene Kendrick Buildings					X
Foster Irradiation Center	X			X	
Gas pump above ground tanks					X
GreenHouse		X			X
Hopkins Hall	X		X		
J.F. Drake Library	X				
Louis Crews Stadium		X			
Mamie Foster Living/Learning	X	X	X		
McCalep Voc Building	X	X			
Morris Hall	X				
Morrison Fine Art	X		X	X	
New Residents Hall	X	X			
Palmer Hall	X				
Patton Hall	X				
Poultry Science	X			X	
R.O.T.C Skills Center	X				
Ralph Lee	X				
School of Business	X		X		
Stephens Hall	X				
Student Health & Wellness Center	X		X		
T.M. Elmore Gym	X				
T.R Parker	X				
T.R. Parker Annex	X				
Terry Hall	X				
Thigpen Hall	X				
Thomas Hall	X				
University Service Building					X
West Campus/ Knight Center	X	X	X		
William Council	X				
Wilson	X				

* Activities (Garage, Maintenance, Chemical Storage, Fuel Storage)
